




US Army Corps
of Engineers®

Mississippi River at Knox Landing

New Orleans District
Last Updated 4/21/2025

Gage Datasheet

Name Mississippi River at Knox Landing
Gage Type DCP
Maintained By U.S. Army Corps of Engineers,
New Orleans District (CEMVN)
USACE Code 01080
Min Height (FT) 18
Max Height (FT) 70
Units of Measure FEET
Installed Date 10/18/1994

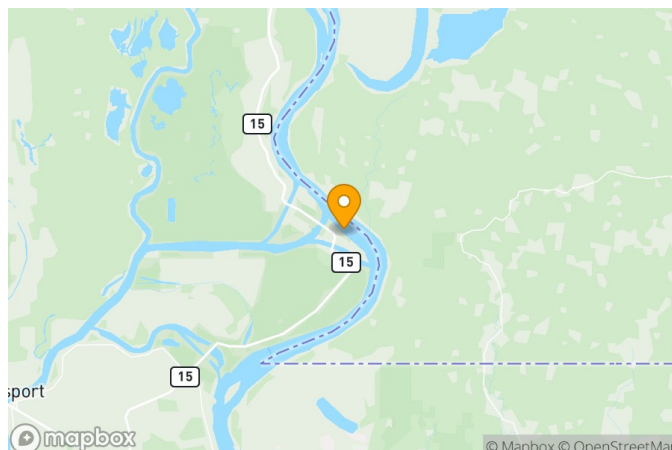

Latitude: 31.07231667 **Longitude:** -91.58275833

Description

(N-4, Mile 311R)

Notes

During flood events, the gage house is moved to the top of levee, so water won't overtake it. Also, min staff gage height changes year to year and more are added as needed.

Gage Calibrations

Vertical Datum	Zero Elevation	Period	Calibration Date	Calibration Divergence Date	Calibration Notes
NGVD29 (1976)	0		1/28/1987		gage set to 0.00 NGVD29 (1976).
NGVD29 (1951)	0		4/3/1958		MSL. First historical record found.

Gage Calibration Adjustments

Calibration Vertical Datum	Target Vertical Datum	Adjustment Factor	Adjustment Start Date	Adjustment End Date	Adjustment Notes
Target Epoch: OPUS					
NGVD29 (1976)	NAVD88	-0.76	9/27/2024		Adjustment of Gage 01080 determined via RTK constrained to primary benchmark LECOQ. Elevation of LECOQ determined via OPUS Shared observation done in Sep 2024. This OPUS observation was done in conjunction with an update of all MVN Mississippi River gages and Primary Control Points (benchmarks) done in late 2024 / early 2025 (EDD-S Job 24-064S). Add the gage adjustment factor to the raw gage reading to determine the NAVD88 value as per OPUS measurement in 2024.
NGVD29 (1976)	NAVD88	-0.08	7/18/2023	9/26/2024	Add -0.08' to gage data adjust from NGVD29 to NAVD88 (OPUS 2019.19) determined using PBM 4GDS elevation = 73.13'; (Geoid12B).
NGVD29 (1976)	NAVD88	-0.07	6/4/2021	7/17/2023	Add -0.07' to gage data to adjust from NGVD29 to NAVD88 (OPUS 2019) determined using TBM # 3 elevation = 50.23'; (Geoid12B)
NGVD29 (1976)	NAVD88	-0.05	9/21/2019	6/3/2021	Add -0.05' to gage data to adjust from NGVD29 to NAVD88 (2019) determined using TBM #3 elevation = 50.23'; (Geoid12B).

Calibration Vertical Datum	Target Vertical Datum	Adjustment Factor	Adjustment Start Date	Adjustment End Date	Adjustment Notes
Target Epoch: 2004.65					
NGVD29 (1976)	NAVD88	-0.22	4/27/2010	9/20/2019	Add -0.22' to gage data to adjust from NGVD29 to NAVD88 (2004.65) determined using BM K254 elevation = 68.60'
Target Epoch: 1967					
NGVD29 (1951)	NGVD29	0.1	11/13/1969	1/27/1987	Add -0.10' to shift data to MSL 1965

Gage Statuses

Status Date	Outside Reference Stage (Feet)	Sensor Stage (Feet)	Sensor Offset Elevation (Feet)	Recorder Stage (Feet)	Precipitation (Inches)	Discharge Calculations Performed	Battery Replacement Performed	Range Maintenance Performed	Equipment Swap Performed	Calibration Survey Performed	Adjustment Survey Performed	Notes
7/18/2023						N	N	N	N	Y	Y	Inspection Done

Gage Equipment

Equipment Type	Equipment Subtype	Model Number	UPC Number	Serial Number	HIF Number	Firmware Version	Installed Date	Removed Date	Remarks
Recorder	Sutron	SL3-ENC-DISP-2		22010898	None	v8.72	5/31/2022	6/13/2024	
Sensor	Bubbler	56-0133-25-1		71475	None		5/31/2022	3/6/2025	
Recorder	Sutron	SL3-ENC-DISP-1		1905171	266043	v8.79	6/13/2024		
Sensor	Bubbler	56-0133-25-1		1601109	238674		3/6/2025		
Sensor	Other	H-340		3109	153986				

Site Photos



Photo of DCP gage house site.
